

THE MASTERPLAN DETERMINES
THE FORM AND LAYOUT OF
WELBORNIE. THE MASTERPLAN
STRUCTURES THE GARDENVILLAGE
INTO A SERIES OF WALKABLE
NEIGHBOURHOODS LINKED BY
AN INTER CONNECTED NETWORK
OF OPEN SPACE AND PEDESTRIAN,
CYCLE AND VEHICULAR ROUTES.
IT IS DESIGNED TO CREATE THE
FRAMEWORK FOR A SUSTAINABLE
NEW COMMUNITY, WHERE PEOPLE
CAN LIVE, WORK AND SHOP.

Four Character Areas: Woodland, Downland, the Meadows and Parkland, based upon existing landscape drivers of the site that give form and identity to the Garden Village.

Movement: An interconnected green network of pedestrian, cycle and vehicular routes based upon a traditional street hierarchy.

Open Space: A spectrum of formal and informal, large and small open spaces linked for sports, recreation and amenity within walking distance of homes, including the 12.5-hectare Welborne Park.



Residential: Up to 6,000 dwellings of a range of types, sizes and tenures.


Parking: Sufficient and convenient residential parking provision, predominantly on-plot to the side of homes plus onstreet.

Social and Community Infrastructure:Three primary schools, one secondary school, healthcare and leisure facilities and community amenities to make for a vibrant and social atmosphere.

Retail and
Employment: Up to
10,000 square metres
of retail space and
up to 105,000 square
metres of business
floor space, including
offices, R&D, industrial
and warehouses to
offer a range of retail
and employment
opportunities within the
Garden Village.

Access: Connected via an upgraded Junction 10 on the M27 to the south and new and existing road junctions with the A32 to the east. M27 Junction 10 Key to unlocking Welborne Garden Village.

Without improvements to Junction 10 only 1160 or so homes can be built

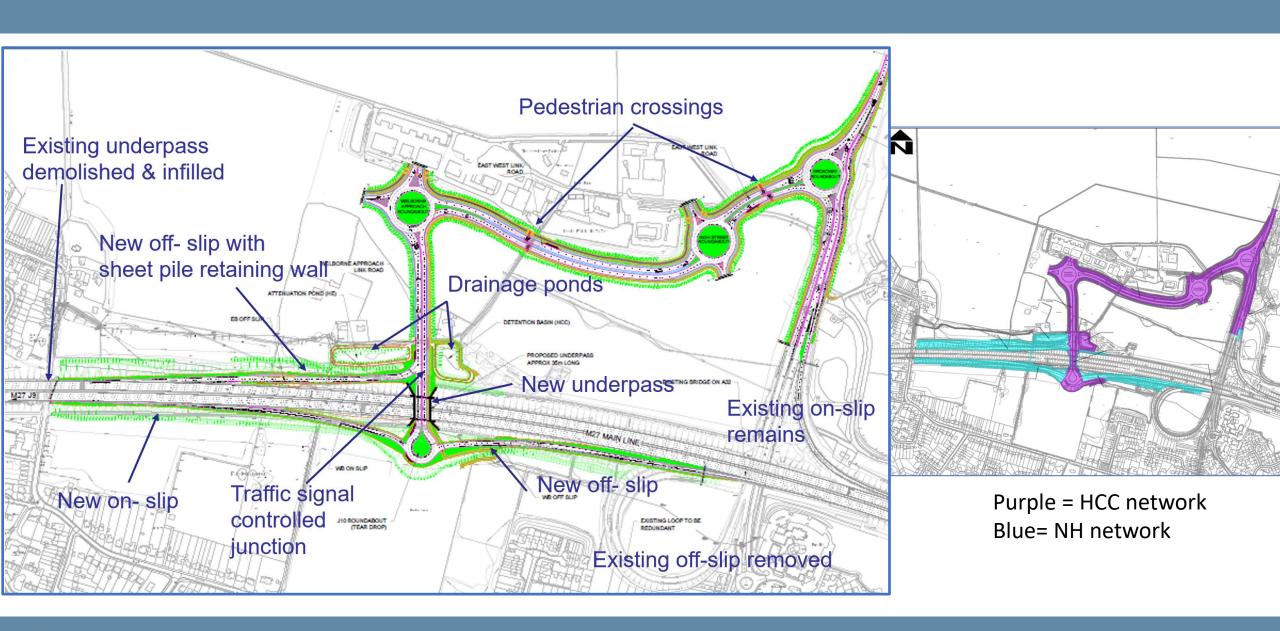

WHO IS INVOLVED?

- 1. NATIONAL HIGHWAYS Highway Authority and approving Authority for SRN,, Land-owner; Sec 6/8 delegation to HCC
- 2. HAMPSHIRE COUNTY COUNCIL Highway Authority and approving Authority for works on local road network, Scheme Promoter, Delivery Body, Funding Agreements with HmE and S106 with WLL; contracting Authority with Design & Build contractor, land access, transfer and dedication agreements, Highway Orders, Licenses for Protected Species
- 3. **DLUHC / Homes England** Housing Infrastructure Grant Funding Agreement / monitoring of conditions
- **4. FAREHAM BOROUGH COUNCIL** Local Planning Authority, granted Planning Permission, S106, Pre-Commencement Planning Condition sign off; HIG Agreement with HmE;
- 5. BUCKLAND DEVELOPMENT LTD Planning Applicant for Welborne Garden Village and Jct 10, submits pre-commencement conditions for Jct 10
- **6. WELBORNE LAND LTD** Land–owner, permits access for construction, transfers and dedicates land to NH and HCC
- 7. VOLKER FITZPATRICK Design and Build Contract with HCC















KEY RECENT PROGRESS

1.	13 July 2021	Cabinet approval for HCC to become Delivery Body
2.	23 Sept 2021	Project Appraisal approved by ELMETE
3.	30 Sept 2021	Planning Permission and S106 Agreed
4.	22 Oct 2021	National Highways/HCC MoU Signed
5.	22 Feb 2022	Section 6/8 Agreement NH/HCC signed
6.	03 March 2022	Grant Determination Agreement for Housing Infrastructure funding signed
7.	08 March 2022	Invitation to Tender released (return 29 April 2022)
8.	05 July 2022	Highway Orders Advertised
9.	15 Aug 2022	Contract sealed with Volker Fitzpatrick (starting date 01 August)
10.	26 Aug 2022	Highway Orders consultation ended


DESIGN AND BUILD CONTRACT

- 8 March 2022 Invitation to Tender released (return 29 April 2022)
- 15 Aug 2022 Contract sealed with Volker Fitzpatrick (starting date 01 August)
- Initial Start Up Meetings taken place throughout August
- Contractor now taking ownership of the Design, Cost Estimate and Programme etc.
- Contract Stage 1 Complete Design and Approvals c 12 months
 - Contract Stage 2 Construct Scheme c 2 years





VolkerFitzpatrick

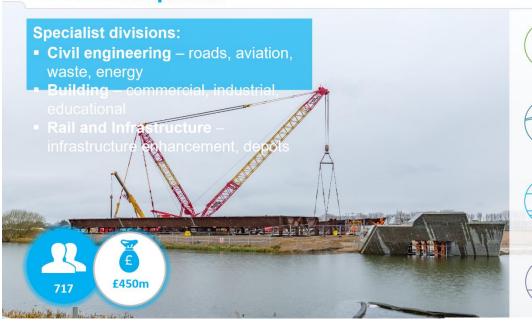












□ Public Realm

Ports



□ Farthworks

☐ Ground Remediation

■ Waste and Energy

















WHAT THE CONTRACTOR IS DOING


Stage 1 Starting Date August 2022
Review Scheme Design, focusing on structure
Secure NH Approvals for Design etc
Completion date not specified subject to NH timescales but will be circa 12 months



Area A – 12 months before agreed completion date

Area B – Spring 2025

Remainder of Works complete – circa Autumn 2025

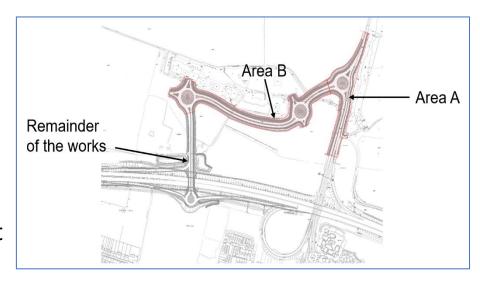


EXAMPLE BOXSLIDE - POTENTIAL APPROACH TO DELIVERY OF STRUCTURE




POTENTIAL APPROACH TO DELIVERY



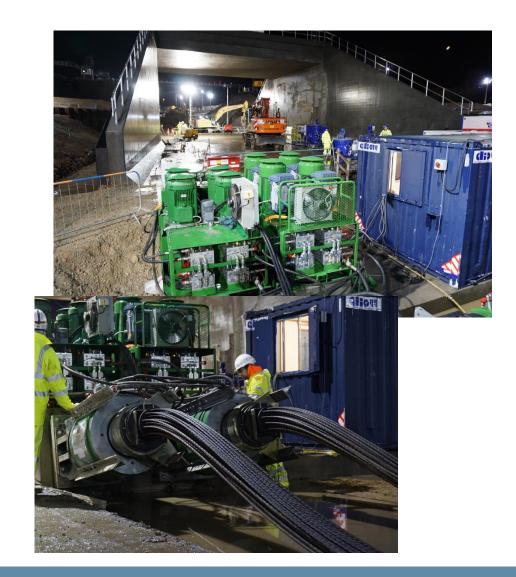

HCC KEY ACTIVITIES – HIGHWAY ORDERS

- 1. **NH / HCC Section 6/8 Agreement -** Delegates Authority to HCC to progress the Highways Orders
- 2. **M27 Junction 10 (Slips Roads Special Roads) and (Side Roads) Highways Orders** consultation commenced 5 July and ended 26 August

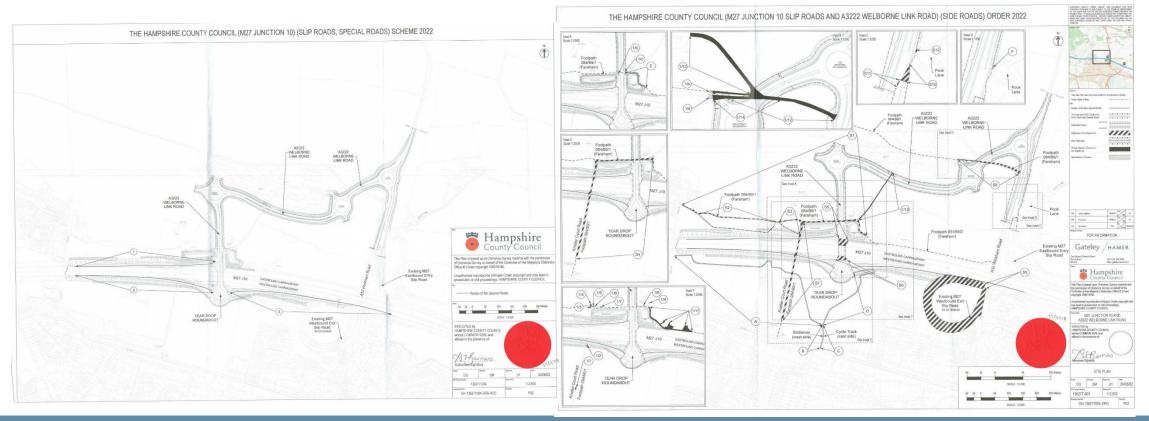

ONGOING ACTIVITIES

LEGAL AGREEMENTS

WLL Access Deed for Temp and Perm Works Land Transfer (WLL to NH); Dedication Agreement (WLL to HCC); Ratification of HCC and NH asset.

PRE-COMMENCEMENT PLANNING CONDITIONS

Part HCC / Part Contractor
Submitted to FBC via BDL
Ecological Management Plan recently submitted and approved
Landscape; lighting, contamination, surface water etc

ADVANCED WORKS

Archaeology Trenching recently completed Licensed work for Badgers, Dormice, GCN, Reptiles, Bats ongoing Arboriculture Impact Assess

